NeuroAIQ
The Neuroscience of AI Adoption


neuroaiq.com.au

SYSTEM MAINTENANCE DOCUMENT

Everything the next team needs to pick this up.

The technical handover for the NeuroAIQ website rebuild. It covers what was built and why, how it fits together, how to run and test it, how to take it live, how to keep it secure and maintained, and what is still to be done. It is written for whoever builds, launches or looks after the site after Team B58.

PREPARED FOR	PREPARED BY	DATE	VERSION
NeuroAIQ Pty Ltd Dr Mahtab Ameri	Team B58, CSE3CAP La Trobe University	13 October 2026	1.1, handover

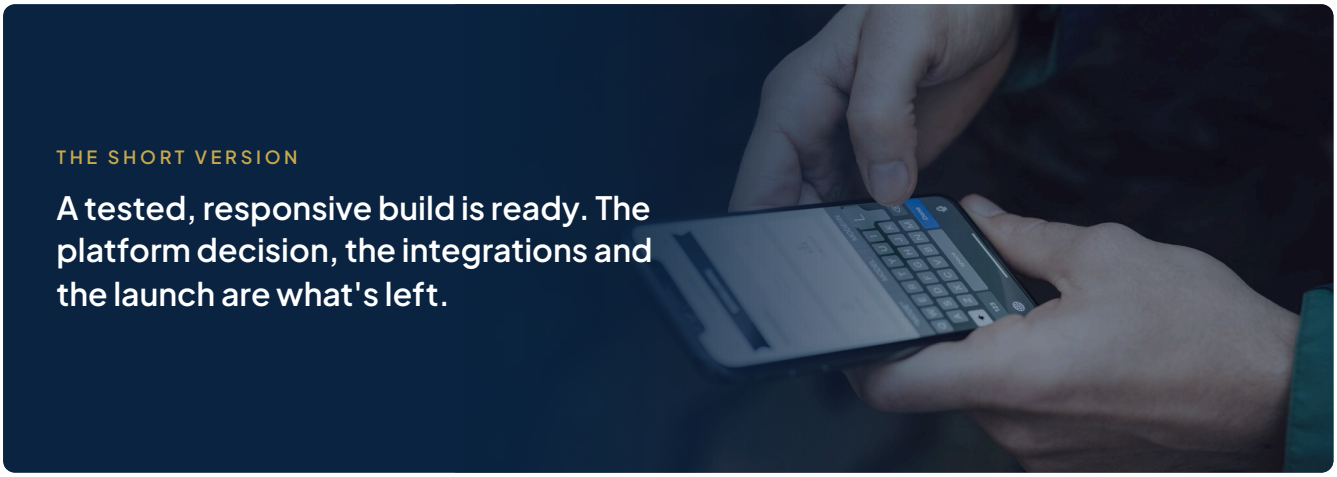

0 Where to start

This document is long because it has to stand on its own. Most readers only need part of it.

IF YOU ARE…	READ
The developer launching or extending the site	Sections 4 to 8, then 11 and 12, and the repository README
Whoever looks after the site once it's live	Sections 9, 10 and 12
NeuroAIQ, deciding what happens next	Sections 1, 3, 13 and 14
An assessor or reviewer	Sections 2, 3 and 11 carry the reasoning and the evidence

Companion documents: User Documentation, Website Security Plan, SEO and AI Search Strategy, Current Website Audit (all Team B58, October 2026).

Contents

1 The project and this handover
2 Requirements: who the site is for and what it must do
3 Design decisions and why we made them
4 System architecture
5 The repository
6 Running and testing
7 From review build to launch
8 Configuration
9 Dependencies and licences
10 Security
11 Testing and known defects
12 Maintenance procedures
13 Future development
14 Open decisions, lessons learned and contacts
A References and glossary

DOCUMENT CONTROL

Version history

VERSION	DATE	CHANGE
0.1	9 August 2026	Website Design and Maintenance Guide issued to the client as a skeleton, with sections marked against the sprint in which they would be written.
1.0	13 October 2026	Replaced by this document at handover. Written against Prototype V3, the client's feedback to 22 September, and the security, SEO and audit documents.
1.1	13 October 2026	Updated for the static build (repository `neuroaiq-website` v1.0.0): architecture, running, testing, deployment and defect status now describe the build, not only the prototype.

AN HONEST NOTE ON STATUS

The rebuilt website **is built and tested but not launched**. Team B58 had no access to the live WordPress site, which is shared with two other student teams, so the build was made as a separate static site from the client-reviewed Prototype V3. It runs as a review copy that search engines can't index. The enquiry form and booking work end to end in review mode but are not yet connected to NeuroAIQ's inbox or calendar. Where something is a recommendation rather than a fact, this document says so.

Which design: the build is made from Prototype V3, the latest version the team had on 13 October. Ahmad Zawi is finishing a further iteration for the client. Because every change made during conversion lives in the converter rather than in the pages, a newer prototype can be carried into the build in under an hour (section 13, "Porting a newer prototype").

1 The project and this handover

NeuroAIQ helps organisations get greater value from their AI investments, by measuring the organisational and workforce conditions that decide whether AI is actually adopted. The website's job is to turn that into enquiries.

Client	NeuroAIQ Pty Ltd, Melbourne. Sponsor and sole approver: Dr Mahtab Ameri, Founder and AI Adoption and Strategy Lead.
Project	Rebuild of neuroaiq.com.au: strategy, content, information architecture, visual design within the existing brand, prototype and deployment.
Primary goal	**Lead generation.** Confirmed by the client on 4 August 2026. Every page is judged on whether it moves a qualified buyer towards a conversation.
Delivery	CSE3CAP Capstone, La Trobe University, Semester 2 2026. Scrum, five sprints from 20 July to 9 October, client review at the end of each.
Constraints	Brand locked (existing logo; navy #003466, electric blue #38B6FF, light gold #C8A84B). No live-site access. Three teams share the project. All work covered by a signed Confidentiality and IP Deed.

WHO DID WHAT

Team B58

MEMBER	ROLES HELD (FROM THE SIGNED TEAM CHARTER, 27 JULY 2026)
Ahmad Zawi	Team lead and client liaison. Front-end and back-end, DNS, contact form. Built the prototype iterations.
Rubayet Mohammad Abdullah	UX and UI design, Figma, front-end, social media and newsletter assets.
Mahmoud Shuqwara	Front-end and back-end, SEO and answer-engine optimisation. Business understanding and competitor research. Handover documentation.
Saif Qasem	Security testing, SEO and AEO support, email marketing. Built the honeypot experiments.
Matthew Axiotis	Security testing and blue-team defence, documentation, copy review to remove machine-sounding text. Maintains the Jira board.

SCOPE OF THE HANDOVER

What is and isn't included

HANDED OVER

- **The website build:** a private Git repository with nine responsive pages, privacy and 404 pages, a test suite and CI
- Prototype V3, the client-reviewed design the build was made from
- This document and the User Documentation
- Website Security Plan, SEO and AI Search Strategy, Current Website Audit
- Business Understanding and Competitor Landscape
- Brand assets, image library and a saved copy of the current live homepage

NOT INCLUDED

- A live deployment on neuroaiq.com.au
- Changes to the current WordPress site
- Account credentials of any kind (none were held by the team)
- Live integrations: the form and booking work in review mode but aren't connected to NeuroAIQ's inbox or calendar; the self-check awaits a client decision
- Final copy for pages the client has not yet approved

HOW WE GOT HERE

Project timeline

WHEN	WHAT HAPPENED
27 Jul	Kickoff. The team presented an outside-in review of the current site, business and competitors.
4 to 9 Aug	Client's nine-point feedback on the brief. Audience, branding and lead generation confirmed. Revised brief and seven planning documents issued.
20 Aug	Early prototypes rejected: invented positioning, missing solutions, generic navigation. Visual work paused to settle strategy.
27 Aug to 11 Sep	Seven areas of business understanding answered in writing; competitor research revisited.
21 to 22 Sep	Prototype V3 sent. Client: "a strong foundation" and "a much stronger narrative", with 12 refinements.
28 Sep to 12 Oct	Security plan, SEO strategy and website audit written and revised for handover.
13 Oct	Static build made from Prototype V3, tested on desktop and phone, and handed over with this document.

2 Requirements: who the site is for and what it must do

These requirements come from the client's own words: her 4 August reply on the brief, her 20 August and 27 August feedback, and her 22 September response to Prototype V3.

BUSINESS OBJECTIVES

What success means for NeuroAIQ

- **Generate qualified enquiries** from organisations adopting or planning to adopt AI.
- **Make the proposition clear in seconds:** why AI investment isn't producing value, why NeuroAIQ is relevant, what is distinctive, what value the buyer gets, and why act now. This is the client's own homepage test.
- **Position NeuroAIQ correctly:** a solution provider that produces evidence, not a change-management or behavioural-change firm.
- **Be findable,** in search engines and in the AI assistants buyers increasingly ask first.

ASSUMPTIONS

What the design takes as given

The primary market is small and medium organisations, so the buyer is often an owner spending their own money. Language must be plain and the first step small.
Buyers research before they call. A senior leader will judge the firm from the homepage and one or two other pages.
DRIVE™ is the entry point to every engagement. Advisory and Workforce Readiness act on the evidence it produces.
The existing brand stays. Our work is layout, typography, imagery and how the existing colours are applied.
Enquiries will be handled in Microsoft 365, HubSpot or both. HubSpot is already installed on the live site.

PERSONAS

Three buyer journeys

The client named ten decision-maker roles. Ten roles can't each have their own path inside this project, so the Lead Generation Strategy grouped them into three journeys. They match the leadership filters on the prototype's Executive Insights page.

LEADING THE BUSINESS

Owner, founder, CEO, MD

Signed the AI invoice and can't see the return. A renewal is coming. Wants a defensible answer quickly, not a six-month programme. Reads the homepage and the DRIVE™ page, then books or leaves.

LEADING AI ADOPTION

Heads of digital, innovation, operations

Owns the rollout. Has usage data but no evidence of value, and suspects Shadow AI. Wants a method they can defend to the executive team. Reads the insights and the case study.

LEADING THE WORKFORCE

HR and People leaders

Training is done but behaviour hasn't changed. Needs to show capability is being built around real work. Reads Workforce Readiness and the Sunway pilot.

USER STORIES

What each visitor needs to be able to do

Status is measured against the build on 13 October 2026. MET is met and tested. PARTIAL works in review mode but isn't connected or final. OPEN needs a client decision or content first. US9 depends on whether the client offers a free tool at all; US11 needs the form handler (section 7); US12 depends on the platform decision (section 4).

ID	AS A… I WANT TO… SO THAT…	ACCEPTANCE CRITERIA	STATUS
US1	As a business owner, I want to understand on the homepage why my AI spend isn't paying back, so I can decide whether to keep reading.	Problem stated above the fold; the five homepage-test questions answered in order on one page.	MET
US2	As any buyer, I want to book a conversation from anywhere on the site.	"Book a consultation" in the header of every page; leads to the booking page in one click. Tested.	MET
US3	As a buyer, I want to pick a time to talk without emailing back and forth.	A live calendar shows real availability and confirms by email.	PARTIAL
US4	As a buyer not ready to book, I want to send a question.	Form collects name, work email, organisation, phone, enquiry type, role, size, stage and message; required fields enforced; enquiry reaches NeuroAIQ; visitor sees a confirmation.	PARTIAL
US5	As a buyer, I want to see how DRIVE™, Advisory and Workforce Readiness connect, so I know where to start.	Solutions shown as a sequence (measure, embed, scale), not a flat list; each has a detail section.	MET
US6	As a sceptical executive, I want evidence it has worked elsewhere.	At least one case study with problem, approach, outcome and evidence; client logos shown only with permission.	PARTIAL
US7	As a buyer, I want to know who is behind the firm.	Founder named with credentials; team shown; links to LinkedIn.	MET
US8	As a buyer researching the problem, I want short answers to specific questions.	Insights filterable by business priority and leadership role; each article answers one question. Filters work and are tested; one article is published.	MET
US9	As a buyer not ready to talk, I want a quick way to gauge where we stand.	A short self-check with an indicative result and a next step.	OPEN
US10	As a buyer on my phone, I want the site to work properly.	Every page usable at 360px wide; Core Web Vitals "good". No sideways scroll on any page (tested); Lighthouse mobile 97, LCP 2.4 s.	MET
US11	As NeuroAIQ, I want every enquiry to arrive safely and its source tracked.	Form to Microsoft 365 or HubSpot only; spam protection; analytics key events. Honeypot built and tested; handler and analytics not yet connected.	PARTIAL


ID	AS A… I WANT TO… SO THAT…	ACCEPTANCE CRITERIA	STATUS
US12	As NeuroAIQ, I want to update events and articles without a rebuild.	Content editable by staff, or by web support within an agreed time.	OPEN

3 Design decisions and why we made them

The design changed more because of what we learned about the business than because of visual preference. This section records the decisions a future team is most likely to question, with the alternatives we considered.

INFORMATION ARCHITECTURE

Nine pages, one route to a conversation

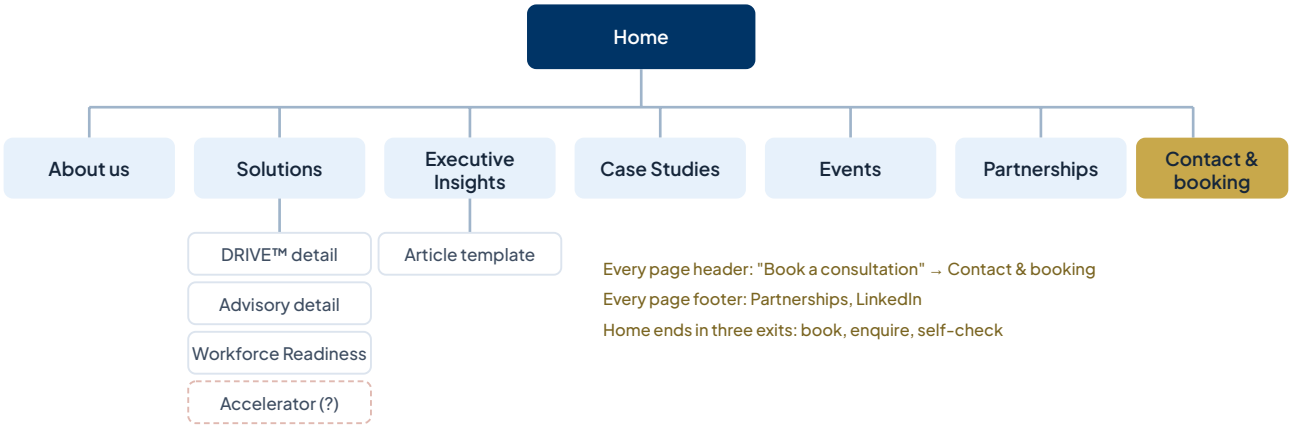

Pages and anchors as built in Prototype V3. The dashed box is the Adaptability Accelerator™, which appears in the prototype but whose status the client has not confirmed.

THE HOMEPAGE

A sequence that answers the client's test

The homepage is built as an argument, in the order a sceptical buyer needs it. Each section has a stated message, purpose, expected buyer response and next step, which is the four-part test the client set on 22 September.

#	SECTION (AS BUILT)	JOB IT DOES
1	The Neuroscience of AI Adoption	Names the category and the firm's angle in one line; two calls to action.
2	The tools are deployed. The value is not arriving.	States the buyer's problem in commercial terms.
3	Four things are already moving inside your organisation.	Urgency from real triggers: renewals, Shadow AI, training without adoption, spend rising.
4	Adoption is not an individual choice. It is a chain of consequences.	LEAD™ as the logic, shown visually, not as a framework to study.
5	Three weeks from question to evidence-based roadmap.	DRIVE™ as the entry point. Speed is a supporting fact, not the headline (client, 22 Sep).
6	Five commercial outcomes, each one measurable.	Protected investment, fewer unused licences, Shadow AI risk found, faster time to value, evidence to prioritise.
7	What it looked like for someone else.	Proof, from the existing case study.
8	Take our AI Adoption Readiness Self-Check	A smaller first step for buyers not ready to talk. Marked work in progress.

#	SECTION (AS BUILT)	JOB IT DOES
9, 10	Written for the people who signed the invoice. / Find out what your AI investment is actually doing.	Who it's for, then the closing call to action.

KEY DECISIONS

Alternatives, trade-offs and what decided it

DECISION	ALTERNATIVES CONSIDERED	WHY WE CHOSE IT, AND THE TRADE-OFF
Strategy before visuals	Keep iterating designs and let positioning emerge	The client rejected the early prototypes because the positioning was invented. We paused visual work and wrote the business understanding first. It cost about three weeks of design time and saved the project.
Prototype as a single HTML design canvas	Build straight into the shared WordPress site; Figma only	No team had live access, and three teams share the site. An HTML canvas let the client review all nine pages side by side in a browser, with real type and real copy. Trade-off: it is a design artefact, not production code (section 7).
One primary call to action	Several equal options: book, enquire, download, subscribe	Lead generation is the point, so "Book a consultation" sits in every header. Enquiry and self-check are secondary exits for buyers not ready to book.
Solutions as a sequence	A grid of equal service cards	The client said a flat list loses the logic. Measure it, embed it, scale it shows DRIVE™ producing the evidence the other two act on.
Remove the 3D brain hero	Animated 3D brain (early prototypes)	The client asked for it to go and for real imagery. The hero now uses a still image so the message loads first.
Qualification fields on the enquiry form	Name, email and message only	Role, organisation size and AI-adoption stage let NeuroAIQ prioritise replies. Trade-off: longer forms convert less, so these sit in an optional, visually separate block.
Booking via a calendar tool	Contact form only; booking link sent privately	Self-service booking removes a round of emails. The prototype marks it optional because the client may prefer to qualify first.
Convert the prototype rather than redraw it	Rebuild every page by hand in a framework	The client had reviewed V3's content and layout, so a script (`tools/convert.py`) carried it across exactly and made it responsive, in hours rather than weeks. Trade-off: page layouts use generated class names (`.s1` to `.s454`) rather than named components. Refactoring them is backlog item 1.
No framework, no build step	React, Next.js, Astro; a WordPress theme	Nine marketing pages don't need one. Plain HTML, CSS and one 15 KB script means nothing to patch, nothing to compile, and any web developer can maintain it. Trade-off: the header and footer are repeated in each page file; a static site generator would remove that if the site grows.
Recommend static hosting	Rebuild on the current WordPress install	Static hosting behind Cloudflare removes the login page, plugins and database, which are where most small-business sites are compromised, and costs less. Trade-off: staff can't edit pages without a developer or a headless CMS. Final call is NeuroAIQ's (section 4).

DESIGN SYSTEM

Colour, type and components


TOKEN	VALUE	USE
Navy	`#003466`	Headings, primary buttons, footer
Electric blue	`#38B6FF`	Accents on dark backgrounds only
Light gold	`#C8A84B`	Highlight button, rules, active tab
Body text	`#4A5A6E`	Paragraphs, navigation
Tint	`#EFF5FB`	Panels, inputs, qualification block

RULES WORTH KEEPING

Typeface: Plus Jakarta Sans, 400 to 800, from Google Fonts.
Contrast: electric blue is only about 2.1:1 on white, so never use it for text on a light background. Use navy, or a darker blue such as `#1272C4`.
Buttons: pill-shaped. Navy for the main action, gold for the hero action.
Sections: numbered eyebrow, then a short headline that makes a claim.

BUYER JOURNEY

How a visitor becomes a conversation



"Book a consultation" sits in every page header, so a ready buyer can skip straight to the gold button from any step.

The journey the homepage and supporting pages are built around. The self-check is dashed because it depends on a client decision.

RISK REGISTER

Design and delivery risks at handover

ID	RISK	L	I	MITIGATION	OWNER
R1	Platform decision drags on and launch stalls	H	H	Section 4 sets out the one deciding question; everything else works either way	NeuroAIQ
R2	No one owns the site after Team B58	H	H	Who-does-what in the security plan; routine in section 12	NeuroAIQ
R3	Known plugin flaws on the live forms are exploited	M	H	Update or remove Fluent Forms, SureForms, AIOSEO now (section 9)	Web support
R4	Copy drifts back to change-management language	M	H	Final copy pass against the "is / is not" list before launch	Build team
R5	Site fails on phones	H*	H	Responsive build, tested at four widths (section 7)	Build team
R6	Spam or leaked enquiry data	M	M	Turnstile, server validation, nothing stored on the web server	Build team
R7	Results or logos published without permission	L	H	Only approved case studies and logos; placeholders removed	NeuroAIQ
R8	Cloudflare blocks AI crawlers and undoes the AEO work	M	M	Check bot settings at launch against the SEO crawler table	Web support
R9	Three teams' changes collide on the live site	M	M	One repository, protected branch, one route to production	Coordinator

L = likelihood, I = impact (high, medium, low). *Certain if the prototype were published as it is.

CHALLENGES

What was hard, and what we'd do differently

- **Positioning took longer than design.** Two months in, the client told us we had invented a positioning. The lesson: get the business understanding in writing and approved before the first wireframe.
- **No live access.** With three teams on one WordPress site, no one could safely build in place. We documented live defects instead of fixing them, and moved the build question to the platform decision.
- **Tests found what review didn't.** The test suite caught two real defects on its first run: the enquiry form stayed on screen after sending, because a component's `display:grid` overrode the `hidden` attribute, and bad phone numbers were accepted, because current Chrome compiles the `pattern` attribute with the regex `v` flag and silently ignored our unescaped pattern. Both are fixed and now covered by tests.
- **Language drifts back.** Words like adaptability and transformation kept returning in copy, even after the client said they make NeuroAIQ read as a change-management firm. Prototype V3 still contained them. The build replaces them, and the changes are listed in the repository's CHANGELOG for the client to approve.

4 System architecture

Three pictures matter: the site as it runs today, the build we hand over, and the production setup we recommend. The platform decision is still NeuroAIQ's to make.

TODAY

The current live site

From public checks on 28 September 2026 and a saved copy of the live homepage in the team's project folder:

Platform	WordPress 6.9.5 on a LiteSpeed server. Theme: Ecliptica 1.0.12. Pages built with Elementor and the Colibri page builder.
DNS and hosting	Hostinger nameservers. HTTPS in place, with a certificate restriction (CAA) record.
Email	Microsoft 365. SPF also authorises HubSpot. DMARC is set to monitoring only (`p=none`).
Marketing and analytics	HubSpot tracking installed. Site Kit by Google installed. Two SEO plugins active at once (Yoast SEO and All in One SEO).
Forms	Three form plugins present (Fluent Forms, SureForms, Spectra forms), plus a quiz plugin.

HANDED OVER

The build


A **static website**: one HTML file per page, two stylesheets and one script, served as finished files with no server code, database or login. That is the "static hosting" option the security plan recommends.

Pages	Home, About, Solutions, Case Studies, Executive Insights, one article, Events, Contact and booking, Partnerships, plus Privacy (draft) and 404
Styles	`site.css` : brand tokens, base, header, footer and every interactive component. `pages.css` : page layouts generated from the prototype, with tablet (≤960px) and phone (≤600px) overrides
Behaviour	`main.js` (no dependencies): mobile menu, insights filters, events tabs, form validation and submission, booking flow, footer year
Assets	26 images converted to WebP and capped at 1600px (7.2 MB → 3.3 MB); fonts self-hosted, so no request goes to Google
Search and AI	Per-page titles and descriptions from the SEO strategy, structured data (organisation, founder, solutions), `sitemap.xml` , a hand-written `llms.txt`
Security	`_headers` sets HSTS, a strict same-origin Content Security Policy, framing protection and the other headers from the security plan
Review mode	`noindex` on every page, `robots.txt` blocking all crawlers, and a footer note; the form and booking confirm on screen without sending

The original Prototype V3 (a single 1240px-wide design canvas) stays in the project folder as the approved design reference. It is not production code.

RECOMMENDED

Production setup

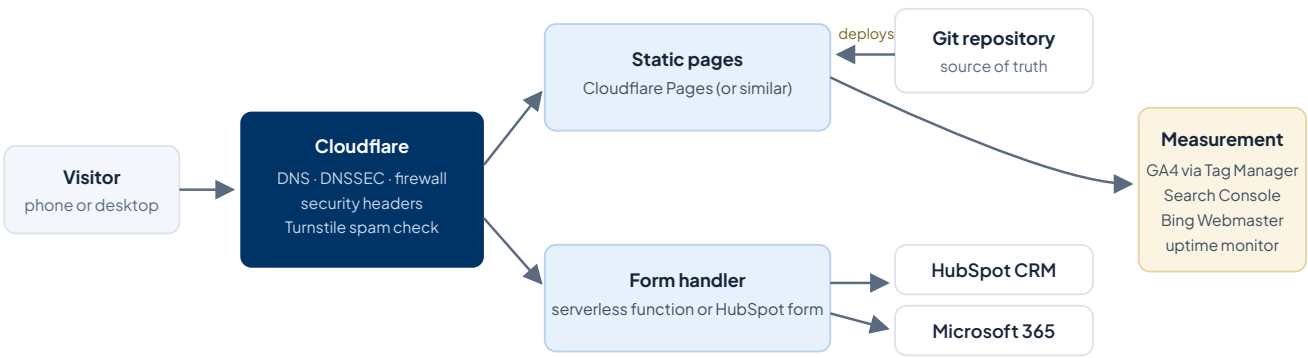

Pages are built from a Git repository and served as static files behind Cloudflare. The only moving part is the enquiry form, which posts to a small handler that delivers to HubSpot and/or Microsoft 365 and stores nothing on the web server.

	STATIC BEHIND CLOUDFLARE (RECOMMENDED)	STAY ON WORDPRESS
Attack surface	Only the files served. No login, plugins or database.	Login page, plugins, themes, database and PHP.
Patching	Rare, only when the site is rebuilt.	Weekly: core, plugins and themes.
Who edits content	Web support, or staff through a headless CMS added later.	Staff, directly in the dashboard.
Running cost	Free to low.	Existing hosting plan, plus plugin licences.
Fits US12 (self-editing)	Only with a CMS or a support agreement.	Yes.

THE DECIDING QUESTION

Does NeuroAIQ need to change pages itself, without a developer? If yes, stay on WordPress and harden it (section 10). If changes are occasional and can go through web support, static hosting is safer and cheaper. Everything else in this document works either way.

5 The repository

Private GitHub repository `neuroaiq-website`, version 1.0.0. Covered by the Confidentiality and IP Deed: keep it private and add collaborators by name.

PATH	WHAT IT IS
`src/`	**The website.** This folder is what gets deployed.
`src/*.html`	One file per page
`src/css/site.css`	Tokens, base, header, footer, every interactive component. Edit by hand.
`src/css/pages.css`	Page layouts generated from the prototype. Edit by hand from now on.
`src/js/main.js`	All behaviour, commented by feature
`src/_headers` , `robots.txt` , `sitemap.xml` , `llms.txt`	Security headers, crawler rules, sitemap, AI summary
`partials/`	The shared layout, header and footer the converter used, and the hand-written privacy and 404 pages
`tools/`	`extract.py` and `convert.py` / `wire.py` : the one-off conversion from Prototype V3. Kept for the record.
`tests/`	Playwright suite (`site.spec.js`) and a zero-dependency preview server (`serve.js`)
`.github/workflows/test.yml`	Runs the suite on every push and pull request
`README.md` , `CHANGELOG.md` , `LICENSE`	Setup, configuration, launch checklist; every change from the prototype (including copy for client approval); licence terms

> DON'T RE-RUN THE CONVERTER
>
> `tools/convert.py` regenerates every page from the prototype export and would overwrite hand edits. It needs `tools/extract.json` and `tools/raw-assets/` , which are git-ignored because they hold the full confidential prototype. Treat the tools as a record of how the site was made, not part of the workflow.

ALSO HANDED OVER

The team's project folder

The shared OneDrive folder holds the reference material: Prototype V3 (`NeuroAIQ Prototype V3 (standalone).html`), the three client documents in `Proposals/` with their HTML sources, the Business Understanding and Competitor Landscape, draft copy in `notes content/` , the logo and image library, and a saved copy of the current live homepage. Superseded explorations (`Landign page templates/` , `Direction A/`) are kept for the record only. Read the Confidentiality and IP Deed in the same folder before sharing anything.

6 Running and testing

The site itself needs nothing installed. Node.js 18 or later runs the preview server and the tests.

RUN IT

Three ways

1. **From disk:** open `src/index.html` in any browser. Every link is relative.
2. **Local server** (recommended, matches production paths):

```
git clone https://github.com/<owner>/neuroaiq-website.git
cd neuroaiq-website
npm install        # test tools only
npm start          # serves src/ on http://localhost:4173
```

3. **Review link:** `https://grand-dodol-927468.netlify.app`, deployed with Netlify Drop on 13 October 2026. Checked live: pages load, fonts and images load, and the CSP, HSTS, framing, content-type and `noindex` headers are all applied. To redeploy, drag the `src` folder onto app.netlify.com/drop.

TEST IT

Before every change goes live

```
npx playwright install chromium   # first time only
npm test                          # 32 tests x 2 devices
npm run test:report               # HTML report with traces for any failure
```

The same suite runs in GitHub Actions on every push and pull request; a red check means don't merge. Section 11 lists what it covers.

7 From review build to launch

The build covers the pages, layout, responsiveness, controls and security headers. What remains is connecting it to NeuroAIQ's systems and switching off review mode.

#	STEP	DETAIL	STATUS
1	Separate pages, real URLs, shared header and footer	Done by the conversion (section 3)	DONE
2	Responsive at every width	Tested at 1280px and on a Pixel 7; no sideways scroll	DONE
3	Real controls and validation	Real `<select>` s, labels, required fields, server-side check still needed (step 6)	DONE
4	Placeholders and copy	Annotations, skeletons and logo slots removed; copy changes listed in CHANGELOG	APPROVE
5	Confirm the platform	Static hosting (as built) or WordPress (section 4)	DECIDE
6	Connect the form	A small handler (for example a Cloudflare Pages Function) that validates again on the server, checks Turnstile, and delivers to HubSpot and/or Microsoft 365. Set its URL in `data-endpoint` on `#enquiry-form` . Keys go in the host's environment variables, never the repository.	TO DO
7	Connect booking	Replace `[data-booking]` with the scheduling tool's embed, or a link sent after qualification	TO DO
8	Measurement	GA4 through Tag Manager, Search Console, Bing Webmaster Tools, the five key events (section 8). Add their domains to the CSP.	TO DO
9	Redirects	A 301 from every old WordPress address to its new page (`_redirects` on Netlify or Cloudflare)	TO DO
10	Switch off review mode	Remove the `noindex` meta, the `X-Robots-Tag` header and the blocking `robots.txt` ; remove the footer review note	AT LAUNCH

DEPLOY

Launch sequence

This follows the security plan's launch steps. Do it in a quiet window: early on a Tuesday or Wednesday morning, Melbourne time.

WHEN	DO THIS
Week before	List every admin account (registrar, hosting, DNS, WordPress, Microsoft 365, HubSpot) and remove anyone who no longer needs access. MFA on all of them. Shared passwords into a password manager. Full backup of the current site, stored off the hosting account.
48 hours before	Lower the DNS time-to-live to five minutes. Write down the rollback: exactly how to point the domain back, and who can call it.
Launch	Deploy, switch DNS, then check from outside (deployment validation below).
After	Keep the old site's backup untouched for at least 30 days. Submit the sitemap to Search Console and Bing.

VALIDATE

Deployment checklist

Launch is finished when every line below has been checked and recorded, not when the new site first appears.

- [ ] Every page loads over HTTPS, with and without `www`, and both land on the same address.
- [ ] SSL Labs grade A, and securityheaders.com grade A. Save both results.
- [ ] A real test enquiry arrives in the right inbox or HubSpot, and the visitor sees a confirmation.
- [ ] A test booking appears in the calendar and sends a confirmation (if booking is live).
- [ ] Every old address redirects to its new page, with no redirect chains.
- [ ] Lighthouse on mobile: Core Web Vitals "good" on the homepage, DRIVE™ and contact pages.
- [ ] robots.txt and the sitemap load, and Cloudflare's AI-crawler blocking matches the SEO strategy's choice.
- [ ] GA4 shows a real-time visit, and the enquiry key event fires once per submission.
- [ ] Uptime and certificate-expiry alerts are on and reach a named person.

ROLL BACK

If launch goes wrong

Point DNS back to the previous host (the low time-to-live means this takes minutes), confirm the old site loads, then work out the cause before trying again. The person allowed to call a rollback is named in the security plan's who-does-what table and must be agreed before launch day.

8 Configuration

Settings that live outside the page code. Each needs a recorded value and an owner. None of them are secrets except where marked; secrets never go in documents or chat.

SETTING	VALUE OR RULE	WHERE IT'S SET
Form endpoint	`data-endpoint` on `#enquiry-form`. Empty = review mode (validates, confirms, sends nothing). Set = POSTs JSON to that URL	contact.html
Indexing (review)	`<meta name="robots" content="noindex">`, `X-Robots-Tag: noindex`, `robots.txt` Disallow: all three come out at launch	Every page, `_headers`, site root
Canonical address	One host, with or without `www`; the other redirects with a 301	Cloudflare / host
DNS time-to-live	5 minutes around launch, then back to the default	DNS provider
SPF	Lists Microsoft 365, HubSpot and the form sender; moves from `~all` to `-all` once DMARC is at reject	DNS TXT record
DMARC	`p=none` with readable reporting, then `quarantine` (week 5), then `reject` (week 8)	DNS TXT record
DNSSEC	On, once DNS moves to Cloudflare	Cloudflare
Form destination	HubSpot and/or Microsoft 365, decided by NeuroAIQ (security plan, question 6)	Form handler
Form keys SECRET	Turnstile secret, HubSpot token, mail credentials	Host environment variables only
Analytics	GA4 property and Tag Manager container owned by a NeuroAIQ Google account, not a student's	Tag Manager
Key events	Enquiry submitted, conversation booked, self-check completed, email or phone clicked, newsletter sign-up	GA4
robots.txt	Allow search and answer crawlers; training crawlers per NeuroAIQ's choice	Site root
Share image	1200 × 627 pixels, set per page	Page head

SECURITY HEADERS

As shipped in `src/_headers`

Netlify and Cloudflare Pages both read this file, so every page carries the headers. The build loads nothing from other sites, so the Content Security Policy is strict: everything same-origin, no inline scripts or styles. When HubSpot, Tag Manager or Turnstile are added, add their domains to the matching directive or they will be blocked.

```
Strict-Transport-Security: max-age=31536000; includeSubDomains
X-Content-Type-Options: nosniff
Referrer-Policy: strict-origin-when-cross-origin
Permissions-Policy: camera=(), microphone=(), geolocation=()
X-Frame-Options: DENY
Content-Security-Policy: default-src 'self'; script-src 'self'; style-src 'self';
  img-src 'self' data:; font-src 'self'; connect-src 'self'; form-action 'self';
  frame-ancestors 'none'; base-uri 'self'
X-Robots-Tag: noindex          # review build only
```

9 Dependencies and licences

Everything the prototype and the current site rely on, and the terms each comes under.

THE BUILD

What ships, and what's only used to test

ITEM	VERSION	LICENCE OR TERMS	SHIPS TO VISITORS?
Plus Jakarta Sans	5.3.0	SIL Open Font Licence 1.1 (`OFL.txt` included)	Yes, self-hosted
Unsplash photos		Unsplash Licence: commercial use, no attribution	Yes, self-hosted
Pixabay images		Pixabay Content Licence: commercial use, no attribution	Yes, self-hosted
Event and team photos, logo		NeuroAIQ's own; confirm consent from people pictured	Yes
Site code	1.0.0	© NeuroAIQ under the IP deed (`LICENSE`)	Yes
@playwright/test	1.56.0	Apache 2.0	No, tests only
@axe-core/playwright	4.10.2	MPL 2.0	No, tests only
Python, BeautifulSoup, Pillow		PSF, MIT, HPND	No, converter only

No JavaScript library ships to visitors, so the build has no third-party runtime code to patch and no CVE exposure of its own. GitHub's Dependabot can watch the two test dependencies.

THE CURRENT SITE

Components found on the live homepage

Versions read from the saved copy of the homepage. They matter if NeuroAIQ stays on WordPress, and for cleaning up the old site if it doesn't.

COMPONENT	VERSION	LICENCE	NOTE
WordPress core	6.9.5	GPLv2+	Keep on automatic updates
Ecliptica theme	1.0.12	GPL	
Elementor	4.1.4	GPLv3	Page builder #1
Colibri Page Builder	1.0.360	GPL	Page builder #2: pick one
Header Footer Elementor	2.9.2	GPL	
All in One SEO	4.9.7.2	GPL	Duplicates Yoast SEO: remove one
Yoast SEO	not shown	GPL	Duplicates AIOSEO
Fluent Forms	6.2.2	GPL	Form plugin #1
SureForms	2.8.0	GPL	Form plugin #2: pick one
Spectra (Ultimate Addons for Gutenberg)	2.20.0	GPL	Includes forms #3
wpDataTables	6.5.1.3	GPL / commercial	Confirm it's used
Quiz Master Next	not shown	GPL	Possibly the earlier self-check
Starter Templates (astra-sites)	not shown	GPL	Setup tool; remove after use

COMPONENT	VERSION	LICENCE	NOTE
Hostinger Reach	not shown	Hostinger	Email subscription block
Site Kit by Google	1.181.0	Apache 2.0	Check whether GA4 is connected
jQuery and jQuery Migrate	bundled	MIT	Ships with WordPress

KNOWN VULNERABILITIES

CVE check, 13 October 2026

Each versioned component was checked against Wordfence Intelligence, Patchstack and the public CVE record. This is a check of version numbers from the saved homepage, not a scan of the live server, and it should be repeated with admin access before any decision is made.

COMPONENT (VERSION)	ADVISORY	ISSUE AND AFFECTED RANGE	RESULT
Fluent Forms (6.2.2)	CVE-2026-16655 CVSS 7.2 High	Unauthenticated stored cross-site scripting through the Name field. All versions up to 6.2.7.	AFFECTED
SureForms (2.8.0)	CVE-2026-7623 CVSS 6.4 Medium	Stored cross-site scripting. Versions up to 2.8.1; fixed in 2.8.2.	AFFECTED
All in One SEO (4.9.7.2)	Wordfence advisory Missing authorisation	Versions before 4.9.9. A related exposure, CVE-2026-5075 (CVSS 4.3, contributor login needed), covers versions up to 4.9.7.	AFFECTED
Elementor (4.1.4)	CVE-2026-57619	Sensitive data exposure, contributor login needed. Up to 4.1.3.	PATCHED
wpDataTables (6.5.1.3)	CVE-2026-57672	Unauthenticated cross-site scripting, CVSS 7.1. Up to 6.5.1.1.	PATCHED
Spectra (2.20.0)	Wordfence advisories	CSS injection before 2.20.0; missing authorisation up to 2.19.22.	PATCHED
Colibri Page Builder (1.0.360)	19 past advisories	Highest affected version listed is 1.0.345.	PATCHED
Quiz Master Next (unknown)	Several, incl. unauthenticated stored XSS up to 11.1.2	Version isn't shown on the page, so it can't be ruled out.	CHECK

WHAT THIS MEANS

Both form plugins have known cross-site scripting flaws, and the Fluent Forms one needs no login. On a site whose job is collecting enquiries, that is the first thing to fix. Update Fluent Forms, SureForms and All in One SEO now, or better, remove the ones that aren't used: keep one form plugin, one SEO plugin and one page builder. Then repeat this check monthly (section 12) and whenever a plugin is added.

10 Security

The Website Security Plan has the full detail. This section maps it to the standards the project follows, so a maintainer can see what each control is for.

OWASP TOP 10 (2021)

The risks that apply to this site

RISK	HOW IT APPLIES HERE	CONTROL
A01 Broken access control	Admin accounts across registrar, DNS, hosting, WordPress, M365, HubSpot	Access audit, one person one account, lowest role, quarterly review
A02 Cryptographic failures	Enquiry data in transit	HTTPS everywhere, HSTS, automatic certificate renewal with expiry alert
A03 Injection	The enquiry form is the only input	Server-side validation, no storage on the web server, output encoding in emails
A04 Insecure design	Collecting more than is needed	Ask only for what's used; phone number optional if not needed to reply
A05 Security misconfiguration	Missing headers, version disclosure, framing allowed	Header set in section 8; hide server and plugin versions
A06 Vulnerable components	Sixteen components on the current site; three with known flaws (section 9)	Cut the list, automatic updates, monthly CVE check (section 9)
A07 Identification and authentication failures	Password guessing on the login page	MFA, limited login attempts, XML-RPC off, or no login at all on static hosting
A08 Software and data integrity failures	Unreviewed changes reaching the live site	Protected branch and pull requests; one coordinated route for all teams' changes
A09 Logging and monitoring failures	Hearing about problems from a prospect	Uptime alerts, Search Console security alerts, readable DMARC reports
A10 Server-side request forgery	Low: the site makes no requests on a visitor's behalf	Keep the form handler to fixed destinations only

AUSTRALIAN BASELINES

Essential Eight, the ASD guide and ISO/IEC 27034

ASD ESSENTIAL EIGHT

Four of the eight apply to a website

MFA on every admin account. **Restrict admin privileges**: one person, one account, lowest role. **Patch applications**: automatic updates and the monthly CVE check. **Regular backups**: daily, off-site, restore tested quarterly. The other four cover staff devices and servers, which the host looks after.

ASD GUIDE AND ISO/IEC 27034

Security built into the lifecycle

Following the ASD software development guidance and the ISO/IEC 27034 idea of application security controls, each control in this document has a stated purpose, an owner and a check that it works: the deployment checklist (section 7), the routine (section 12) and the yearly independent review.

PRIVACY

Enquiry data

The form collects names, work emails, phone numbers and what people say about their organisation's AI problems. Whether or not the Privacy Act 1988 formally applies to NeuroAIQ, handle it as though it does: a published privacy policy (what's collected, why, where it's kept, how to ask for deletion), analytics and advertising pixels disclosed, nothing passed to ad platforms. If a breach is likely to cause serious harm and the Act applies, it must be reported to the OAIC and the people affected under the Notifiable Data Breaches scheme.

SECURITY IN THE BUILD

What's already in place

No login, database or server code; strict CSP and framing protection; every form field validated in the browser, with a hidden honeypot field that silently drops bot submissions; no enquiry data stored anywhere in review mode. Server-side validation and Turnstile come with the form handler (section 7, step 6).

TEAM TESTING

What was tested, and what wasn't

Checks of the live site on 28 September were passive: public response headers and DNS records only. No active testing was run against neuroaiq.com.au, because it is shared and in production. As part of the security work, Saif Qasem built a honeypot (a decoy that flags automated attacks) on 7 October. It is not part of this handover, and any decoy should be reviewed with NeuroAIQ before it goes anywhere near the live site.

11 Testing and known defects

Two kinds of testing happened: the client reviewed each version against her own criteria, and the team ran automated checks on the final prototype.

ACCEPTANCE TESTING

Client reviews

DATE	VERSION	RESULT
20 Aug 2026	Early prototypes	REJECTED Ten concerns, led by invented positioning and missing solutions.
27 Aug 2026	Strategy	REWORK Seven areas of business understanding to demonstrate first.
22 Sep 2026	Prototype V3	ACCEPTED IN PRINCIPLE "A strong foundation" and "a much stronger narrative". Twelve refinements: buyer journey, premium benchmarking, visual language.

BEFORE

Prototype V3, checked 13 October 2026

The prototype was rendered in headless Chromium at 1400 × 900 and 390 × 844. All nine frames rendered, 105 internal links resolved and all 40 images had alt text, but: the form could be "sent" empty (no `required`), the drop-downs were drawn shapes, nothing was submitted, and at 390px the document was 16,400px wide. Those findings set the build's acceptance tests.

AFTER

The build: automated test suite

64 of 64 passing on 13 October 2026: 32 Playwright tests, each run on a 1280px desktop and an emulated Pixel 7 phone.

AREA	WHAT'S CHECKED	RESULT
Every page (10)	Loads; one `<h1>`; title and description; every image loads and has alt text; no sideways scroll; no em dashes; no console errors	PASS
Accessibility (10)	axe-core, WCAG 2 A and AA: no serious or critical violations	PASS
Links	Every internal link and `#anchor` on every page resolves	PASS
Navigation	Mobile menu opens, closes on Escape; current page marked; booking one click away	PASS
Insights filters	Priority filter, role filter, empty state, reset; only the published article links	PASS
Events tabs	Mouse and arrow keys; correct panel shown	PASS
Enquiry form	Six required errors and focus on the first; bad email and phone caught and cleared; confirmation; honeypot	PASS
Booking	Person, date, time, details (validated), confirmation; no weekends or past dates	PASS
Review mode	`noindex` present; `robots.txt` blocks crawlers	PASS

PERFORMANCE

Lighthouse 12.2.1

PAGE	DEVICE	PERFORMANCE	ACCESSIBILITY	BEST PRACTICES	SEO	LCP	CLS
Home	Mobile	97	100	100	66*	2.4 s	0
Home	Desktop	100	100	100	66*	0.5 s	0
Contact	Mobile	97	100	100	66*	2.4 s	0
Contact	Desktop	100	100	100	66*	0.5 s	0

*SEO is capped only by the deliberate `noindex` on the review build; every other SEO audit passes. Run on a local server; rerun on the production host after launch. The first mobile run had LCP at 3.0 s; marking the hero image `fetchpriority="high"` brought it to 2.4 s, inside Google's "good" threshold of 2.5 s.

USABILITY

Testing with people, 13 October 2026

Five people outside the team (two business owners, one manager, two students) used the review link on a laptop (2), phone (2) or tablet (1), tried six tasks and answered an anonymous Google Form. **26 of 30 task attempts succeeded** (18 easily, 8 with effort), **average ease 4.2 of 5**, and all five recognised within ten seconds that NeuroAIQ works in AI; three called it a consultancy, one "AI adoption". The hardest task was finding upcoming events (2 of 5 easily): the empty tab read as broken. Both forms were described as asking for "lots of information", and one phone user, the lowest-rated session, couldn't find the founder, an article, booking or events. Full results and recommended changes are in the User Documentation, section 5. Small, self-selected sample: an early signal, not a verdict.

DEBUGGING

Defects the tests found, and the fixes

SYMPTOM	CAUSE	FIX
Form stayed visible after a successful send	The component rule `.enquiry{display:grid}` outranked the browser's default for the `hidden` attribute	Global `[hidden]{display:none!important}`; covered by a test
"abc" accepted as a phone number	Chrome now compiles `pattern` with the regex `v` flag, where `( ) + -` must be escaped in a character class; the invalid pattern was silently ignored	Escaped pattern; covered by a test
Booking panel layout broken	The converter turned the wrong element into the "person" button, pulling the panel out of its grid	Select the whole card by its role line
Converter crashed removing placeholders	Removing a parent inside a loop over its own children	Re-query after each removal

DEFECT REGISTER

Status at handover

ID	DEFECT (FROM THE PROTOTYPE REVIEW)	STATUS
D1	Layout not responsive	FIXED
D2	Form fields not enforced; drop-downs not real controls	FIXED
D3	Form, booking and self-check not connected	REVIEW MODE
D4	Placeholders (logo boxes, "to be supplied" notes, event rows, approval note)	FIXED
D5	Change-management wording ("adaptability", "transformation") in copy	FIXED, NEEDS APPROVAL
D6	Navigation differed on Case Studies	FIXED
D7	Footer "© 2025"	FIXED
D8	Em dashes in copy	FIXED, TESTED
D9	™ and ® symbols not used consistently	CLIENT DECISION
D10	*New:* page layouts use generated class names	BACKLOG #1
D11	*New:* only one of twelve insights pieces is written	CONTENT
D12	*User testing:* empty Upcoming events tab reads as broken	BACKLOG
D13	*User testing:* booking and enquiry feel long ("requires lots of information")	BACKLOG
D14	*User testing:* founder hard to find on a phone; "AI adoption" not landing in ten seconds	BACKLOG

12 Maintenance procedures

Once launch week is over, looking after the site takes about an hour a month for security, plus the content routine. Each task needs a named owner after handover.

ROUTINE

The calendar

HOW OFTEN	SECURITY AND OPERATIONS	CONTENT AND SEARCH
Weekly 5 minutes	Glance at uptime alerts. On WordPress, confirm updates ran.	Reply to every enquiry within two business days, which the contact page promises.
Monthly 1 to 2 hours	Re-run SSL Labs and securityheaders.com. Check backups ran. Read the DMARC summary. CVE check (section 9).	Two articles. One-page report: enquiries by source, top searches, pages indexed. Ask the monthly question set in five AI assistants and record whether NeuroAIQ is named.
Quarterly 1 hour	Restore a backup to a test address and check it. Review who has access.	Update the events page. Check every page title still matches the page.
Yearly half a day	Independent security review. Rotate key passwords. Revisit the security plan.	Review the page list and redirects. Recheck how AI assistants find sources.

HOW TO

Common changes

TASK	STATIC HOSTING	WORDPRESS
Change text on a page	Edit `src/<page>.html` in a branch, run `npm test`, open a pull request; CI runs the tests and the host builds a preview link; merge to publish.	Pages → edit → Update. Check on a phone.
Add an article	Copy `insights-should-we-keep-investing-in-ai.html`, change the title, description and body; on `insights.html` turn the matching card back into a link; add the URL to `sitemap.xml` and the page list in `tests/site.spec.js`.	Posts → Add new; set category, SEO title, description and share image.
Add an event	In `events.html`, copy an event card into the right panel (`#panel-past`, `#panel-current` or `#panel-upcoming`) and remove that panel's "nothing on" message.	Edit the Events page.
Replace an image	Save as WebP under 300 KB in `src/assets/img/`, set `width`, `height` and alt text; the image test fails if alt is missing.	Same, through the media library.
Remove a page	Delete it, then add a 301 redirect from its address to the closest page.	Same, using the SEO plugin's redirect tool.

TROUBLESHOOTING

For whoever looks after the site

SYMPTOM	LIKELY CAUSE	FIRST MOVE
Enquiries stopped arriving	Handler or mail credentials changed; mail filtered after a DMARC change	Send a test enquiry; check spam and HubSpot; check the handler's logs
Browser shows a security warning	Certificate failed to renew	Check the expiry alert; renew at Cloudflare or host
A service stopped working after a header change	Content Security Policy blocking it	Read the browser console; add the domain to the right directive
Site down	Host outage, DNS change, failed deploy	Check the host status page; roll back the last deploy
Rankings dropped after a change	Missing redirects, page de-indexed, robots.txt edited	Search Console coverage report; recheck redirects and robots.txt
AI assistants stopped naming NeuroAIQ	Crawlers blocked at Cloudflare	Check bot settings against the SEO strategy's crawler table
Strange content or redirects appear	Compromise	Follow the incident runbook below

INCIDENT RUNBOOK

Five moves, in this order

1. **Contain.** Take the site offline or to a holding page. Change passwords.
2. **Assess.** What happened, what data was involved, and since when.
3. **Restore** from the last backup known to be clean, which isn't always the latest.
4. **Notify.** If personal data was involved, work out who must be told (OAIC, people affected). Cyber incidents can be reported to the ACSC through ReportCyber at cyber.gov.au.
5. **Learn.** Write up what happened, fix the cause, update this document.

13 Future development

A prioritised backlog for the next team. Priority 1 is needed for launch; priority 2 in the first three months; priority 3 when there's data to justify it.

P	ITEM	WHY, AND HOW TO EXTEND
1	Port the next prototype iteration	Ahmad Zawi's iteration in progress at handover. Procedure below; about an hour if the structure holds.
1	Connect the enquiry form	The site's main job. Pages Function or HubSpot Forms API, server-side validation, Turnstile; set `data-endpoint` .
1	Client approval of copy changes	Seven changes listed in CHANGELOG.md.
1	SEO and measurement at launch	Remove review mode, redirects, GA4 key events, Search Console and Bing. Baseline from day one.
1	Act on user testing	D12 to D14: a clearer Upcoming empty state, collapse optional form fields, founder line and "AI adoption" in the Home hero. Re-test with three to five target buyers.
2	Refactor `pages.css`	Replace generated classes with named components (section, eyebrow, card, stat), one page at a time. The tests and screenshots catch regressions.
2	Booking	Connect a scheduling tool, or replace with a private link sent after qualification.
2	Articles and problem pages	The flagship guide and ten articles show "coming soon". Each opens with a one-paragraph answer (SEO strategy, Part three).
2	DRIVE™ week-by-week	Needs the client's breakdown of the three weeks; the build removed the empty placeholders.
3	Self-check	If approved: five to eight questions, an indicative result, a link to book; answers stored only with consent.
3	Templating or a headless CMS	If pages multiply, move the header and footer into a static site generator, or add a Git-based CMS so staff edits arrive as pull requests.
3	Lighthouse CI budget	Fail the build if mobile performance drops below 90 on the production domain.

PORTING A NEWER PROTOTYPE

When the next iteration arrives

No page has been edited by hand since conversion: every fix lives in `tools/wire.py` , `partials/` , `site.css` and `main.js` . So a newer prototype from the same design tool can be carried across by re-running the pipeline:

```
python tools/extract.py "NeuroAIQ Prototype V4 (standalone).html"
python tools/convert.py      # rewrites src/*.html and pages.css
npm test                     # 64 checks on desktop and phone
git diff --stat              # review what changed, page by page
```

The wiring finds elements by their visible text (for example "Select a date and time"). If a heading is reworded, update the matching line in `wire.py` ; a failing test will say which. Re-check the CHANGELOG's copy table against the new wording. Once anyone edits a page by hand, stop using the converter and port changes manually.

> EXTENDING WITHOUT BREAKING IT
>
> New pages reuse an existing template and the tokens in section 3. Each new page needs a title, a description, a share image, a place in the sitemap and a single next step. Before anything new goes live, it passes the client's four-part test: message, purpose, buyer response, next step.

14 Open decisions, lessons learned and contacts

These are genuine gaps, not assumptions we chose not to make. The first two shape everything else.

#	DECISION FOR NEUROAIQ	WHAT IT CHANGES
Now	**Update or remove Fluent Forms, SureForms and All in One SEO on the current site.** They have known flaws (section 9) and don't need to wait for the rebuild.	Security of today's enquiries
1	Static hosting or WordPress? The build is ready for static hosting as it stands.	Security work, editing, cost (section 4)
2	Who builds, launches and maintains the site after Team B58?	Every owner column in this document
3	Offer a free self-check? If so, its name: "AI Adoption Readiness Self-Check" (prototype, SEO strategy) or "DRIVE Scorecard" (design strategy draft)	US9, the home page's closing exits
4	Use ® and ™ symbols on the new site?	D9, all copy
5	Is the Adaptability Accelerator™ current, planned or retired?	Solutions page; its old URL returns a 404
6	Enquiries to HubSpot, Microsoft 365, or both?	Form handler, SPF
7	Which case-study results and client logos can be published?	US6
8	Approve the seven copy changes in the build's CHANGELOG	D5, launch

LESSONS LEARNED

For the next student team on a client project

- Write down the client's own description of the business and get it approved before designing anything.
- Agree on day one how several teams will get changes onto one live site.
- Keep a single list of client feedback and check every version against all of it, not just the latest email.
- Treat words as a requirement. The client's "is / is not" list mattered as much as any layout.

CONTACTS

At handover

Client sponsor	Dr Mahtab Ameri, NeuroAIQ · mahtab.ameri@neuroaiq.com.au
Team B58 liaison	Ahmad Zawi · 20753581@students.latrobe.edu.au
This document	Mahmoud Shuqwara · 22177153@students.latrobe.edu.au
Subject coordinator	Dr Scott Mann, La Trobe University · s.mann@latrobe.edu.au

Student addresses may close after graduation. Questions after that go through NeuroAIQ.

A References and glossary

- OWASP Foundation. *OWASP Top 10: 2021.* owasp.org/Top10
- Australian Signals Directorate. *Essential Eight Maturity Model.* cyber.gov.au
- Australian Signals Directorate. *Secure software development guidance,* March 2024. cyber.gov.au
- ISO/IEC 27034-1:2011. *Application security: overview and concepts.*
- Office of the Australian Information Commissioner. *Notifiable Data Breaches scheme.* oaic.gov.au
- Google. *Core Web Vitals.* web.dev/vitals
- Team B58. *Website Security Plan; SEO and AI Search Strategy; Current Website Audit,* v1.1, 12 October 2026.
- Team B58. *Business Understanding; Competitor Landscape,* September 2026.

AEO	Answer-engine optimisation: being quoted by AI assistants.
CSP	Content Security Policy: a header listing where a page may load code from.
CVE	A publicly catalogued software vulnerability.
DMARC	An email setting that tells receivers what to do with mail that fails the domain's checks.
DRIVE™	NeuroAIQ's Adaptability Diagnostic; the entry point to every engagement.
LEAD™	NeuroAIQ's logic from leadership decisions to business value.
Static site	Pages served as finished files, with no database or login.
TTL	Time-to-live: how long DNS answers are cached.

HANDOVER

Built on the client's own words, and written so the next team can carry it the rest of the way.

NeuroAIQ
The Neuroscience of AI Adoption
